

DUCT SEALING REPORT

Duct Sealing Performed For:



DATE: 11/5/2021

Overall Sealing Results:

BEFORE SERVICE

643.9 CFM of Leakage, equivalent to a 121.7 Square Inch Hole or 54% of the system capacity of 1200.0 CFM

AFTER SERVICE

13.5 CFM of Leakage, equivalent to a 2.6 Square Inch Hole or 1.1% of system capacity

> This corresponds to a 98% Reduction in Duct Leakage

NOTE: Duct leakage results are calculated in Cubic Feet per Minute (CFM) measured at a STANDARD OPERATING PRESSURE of 25 Pa.

Duct Sealing Performed By:

Comfort Heating & Cooling 221 E Grant St Augusta, Wisconsin 54722 Phone: 7158293231

Aeroseal process uses DuctSeal sealant that is certified to meet requirements listed in UL 1381 standard-"Outline of investigation for Aerosol Duct Sealant" Please provide Aeroseal feedback at http://bit.ly/2021aeroseal and reference code NPKUQQQ.

Aeroseal Sealing Progress:


AEROSEAL CASE ID: 5536

SYSTEM DESCRIPTION: Basement HVAC

SEAL DESCRIPTION: Whole Home seal

HARDWARE: HomeSeal Connect

TECHNICIAN: Roland

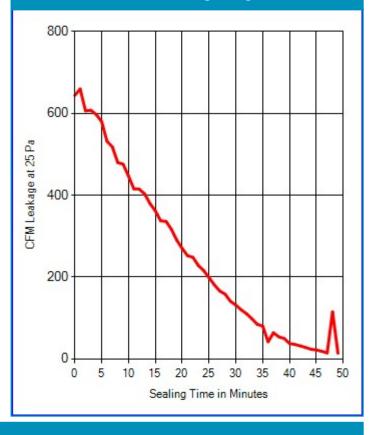

×
